



ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 18, '07							Nov 25, '07			
							F	S	S	M	T	W	T	F	S	S	M
1	1 Initiation	41 days	Sat 11/17/07	Sat 1/12/08													
2	1.1 Realize Problem	1 hr	Sat 11/17/07	Sat 11/17/07		Keith01											
3	1.2 Kickoff Meeting	1 hr	Fri 1/11/08	Fri 1/11/08	2FS+40 day	Keith01,Keith02,Keith03											
4	1.3 Develop Project Charter	2 days	Fri 1/11/08	Sat 1/12/08	3	Keith01[10%]											
5	1.4 Charter signoff	0 days	Sat 1/12/08	Sat 1/12/08	4	Keith01,Keith02,Keith03											
6	2 Investigation	0 days	Sat 5/24/08	Sat 5/24/08													
7	2.1 Access old computer	0 days	Sat 5/24/08	Sat 5/24/08													
8	2.1.1 Use CPU-Z to determine hardware	15 mins	Sat 5/24/08	Sat 5/24/08	5FS+96 days	Keith02											
9	2.1.2 Check hardware	0 days	Sat 5/24/08	Sat 5/24/08													
10	2.1.2.1 turn off computer	15 mins	Sat 5/24/08	Sat 5/24/08	8	Keith03											
11	2.1.2.2 Unplug computer	10 mins	Sat 5/24/08	Sat 5/24/08	10	Keith03											
12	2.1.2.3 Open computer up	1 hr	Sat 5/24/08	Sat 5/24/08	11	Keith03											
13	2.1.2.4 See if anything is salvage	1 hr	Sat 5/24/08	Sat 5/24/08	12	Keith03											
14	2.1.2.5 close computer up	1 hr	Sat 5/24/08	Sat 5/24/08	13	Keith03											
15	2.1.2.6 plug computer back in	1 hr	Sat 5/24/08	Sat 5/24/08	14	Keith03											
16	3 Planning	0.46 days	Sat 5/24/08	Sun 5/25/08													
17	3.1 Develop project plans	6 hrs	Sat 5/24/08	Sun 5/25/08	15	Keith01											
18	3.2 Review project plans	1 day	Sun 5/25/08	Sun 5/25/08	17	Keith02,Keith03											
19	3.3 Approve project plans	0 days	Sun 5/25/08	Sun 5/25/08	18	Keith01,Keith02,Keith03											
20	4 Executing	17.54 days	Sun 12/14/08	Sat 1/3/09													
21	4.1 Order parts	0.13 days	Sun 12/14/08	Sun 12/14/08													
22	4.1.1 Go to New Egg for components	1 hr	Sun 12/14/08	Sun 12/14/08	19FS+146 days	Keith01											
23	4.1.2 Go to Amazon for anti-static mat	1 hr	Sun 12/14/08	Sun 12/14/08	22	Keith01											
24	4.1.3 Ordering complete	0 days	Sun 12/14/08	Sun 12/14/08	23	Keith01											
25	4.2 Build Computer	5.92 days	Sun 12/28/08	Sat 1/3/09													
26	4.2.1 Open boxes to get manuals	3 hrs	Sun 12/28/08	Sun 12/28/08	24FS+11 days	Keith01											
27	4.2.2 Read manuals	1 hr	Sun 12/28/08	Sun 12/28/08	26	Keith01[10%],Keith02											
28	4.2.3 Lay down anti-static mat	1 hr	Sun 12/28/08	Sun 12/28/08	27	Keith03,anti-static mat[1]											
29	4.2.4 Salvage components from old computer	0 days	Sun 12/28/08	Sun 12/28/08													
30	4.2.4.1 Remove DVD burner	1 hr	Sun 12/28/08	Sun 12/28/08	28	Keith03,Plextor D											
31	4.2.4.2 Get keyboard and mouse	1 hr	Sun 12/28/08	Sun 12/28/08	30	keyboard/mouse[1]											
32	4.2.5 Build new computer	0 days	Sun 12/28/08	Mon 12/29/08		Keith03											
33	4.2.5.1 Place new case on anti-static mat	1 hr	Sun 12/28/08	Sun 12/28/08	31	Cooler Master Centurion											
34	4.2.5.2 Install power supply	15 mins	Sun 12/28/08	Sun 12/28/08	33	Keith03,COOLEF											
35	4.2.5.3 Install custom motherboard back plate	4 mins	Sun 12/28/08	Sun 12/28/08	34	Keith03											

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 18, '07							Nov 25, '07			
							F	S	S	M	T	W	T	F	S	S	M
36	4.2.5.4 Set up motherboard for install in case	0 days	Sun 12/28/08	Sun 12/28/08													
37	4.2.5.4.1 Set motherboard	5 mins	Sun 12/28/08	Sun 12/28/08	35	Keith03,Asus P6											
38	4.2.5.4.2 Install CPU	5 mins	Sun 12/28/08	Sun 12/28/08	37	Keith03,Intel Cor											
39	4.2.5.4.3 Install CPU cooler	10 mins	Sun 12/28/08	Sun 12/28/08	38	Keith03											
40	4.2.5.4.4 Install RAM	10 mins	Sun 12/28/08	Sun 12/28/08	39	Keith03,1) G.Skil											
41	4.2.5.4.5 Motherboard complete	0 days	Sun 12/28/08	Sun 12/28/08	40	Keith03											
42	4.2.5.5 Install motherboard	30 mins	Sun 12/28/08	Sun 12/28/08	41	Keith03,Asus P6											
43	4.2.5.6 Install video card	4 mins	Sun 12/28/08	Sun 12/28/08	42	Keith03,HIS Rad											
44	4.2.5.7 Install sound card	4 mins	Sun 12/28/08	Sun 12/28/08	43	Keith03,Creative											
45	4.2.5.8 Install hard drives	30 mins	Sun 12/28/08	Sun 12/28/08	44	Keith03,1) Weste											
46	4.2.5.9 Install DVD Burner	15 mins	Sun 12/28/08	Sun 12/28/08	45	Keith03,Plextor D											
47	4.2.5.10 Wire up case front to motherboard	20 mins	Sun 12/28/08	Mon 12/29/08	46	Keith03											
48	4.2.5.11 Plug keyboard and mouse in	2 mins	Mon 12/29/08	Mon 12/29/08	47	Keith03,keyboard											
49	4.2.5.12 Plug monitor in	5 mins	Mon 12/29/08	Mon 12/29/08	48	Keith03,Dell 1704											
50	4.2.5.13 Plug speakers in	2 mins	Mon 12/29/08	Mon 12/29/08	49	Keith03											
51	4.2.5.14 Plug system in	1 min	Mon 12/29/08	Mon 12/29/08	50	Keith03											
52	4.2.5.15 Turn power on	1 min	Mon 12/29/08	Mon 12/29/08	51	Keith03											
53	4.2.5.16 Turn power off	1 min	Mon 12/29/08	Mon 12/29/08	52	Keith03											
54	4.2.5.17 Close system up	10 mins	Mon 12/29/08	Mon 12/29/08	53	Keith03											
55	4.2.5.18 Hardware complete	0 days	Mon 12/29/08	Mon 12/29/08	54	Keith03											
56	4.2.6 Install Software	5.5 days	Mon 12/29/08	Sat 1/3/09													
57	4.2.6.1 Flash BIOS	1 hr	Mon 12/29/08	Mon 12/29/08	55	Keith03											
58	4.2.6.2 Install Windows XP SP3	3 hrs	Mon 12/29/08	Mon 12/29/08	57	Keith02											
59	4.2.6.3 Install Windows Vista Ultimate x64	2 hrs	Mon 12/29/08	Mon 12/29/08	58	Keith02											
60	4.2.6.4 Install Ubuntu 8.10	1 hr	Mon 12/29/08	Mon 12/29/08	59	Keith02											
61	4.2.6.5 Operating System installs complete	0 days	Mon 12/29/08	Mon 12/29/08	60	Keith02											
62	4.2.6.6 Windows XP SP3 Software	0 days	Fri 1/2/09	Sat 1/3/09													
63	4.2.6.6.1 Install Office 2007	1 hr	Fri 1/2/09	Fri 1/2/09	61FS+5 days	Keith02											
64	4.2.6.6.2 Install Visual Studio 2005	3 hrs	Fri 1/2/09	Fri 1/2/09	63	Keith02											
65	4.2.6.6.3 Install Visual Studio 2008	3 hrs	Fri 1/2/09	Sat 1/3/09	64	Keith02											
66	4.2.6.6.4 Install Java JDK and Eclipse	30 mins	Sat 1/3/09	Sat 1/3/09	65	Keith02											
67	4.2.6.6.5 Install Notepad++	5 mins	Sat 1/3/09	Sat 1/3/09	66	Keith02											
68	4.2.6.6.6 Essential software installs complete	0 days	Sat 1/3/09	Sat 1/3/09	67	Keith02											

ID	Task Name	Duration	Start	Finish	Predecessor	Resource Names	Nov 18, '07							Nov 25, '0		
							F	S	S	M	T	W	T	F	S	S
69	4.2.6.6.7 Install Firefox	10 mins	Sat 1/3/09	Sat 1/3/09	67	Keith01										
70	4.2.6.6.8 Install Baldur's Gate II	1 hr	Sat 1/3/09	Sat 1/3/09	69	Keith01										
71	4.2.6.6.9 Install Freedom Force	30 mins	Sat 1/3/09	Sat 1/3/09	70	Keith01										
72	4.2.6.6.10 Install Freedom Force vs. 3rd Reich	30 mins	Sat 1/3/09	Sat 1/3/09	71	Keith01										
73	4.2.6.6.11 Install Star Wars: Knights of the Old	1 hr	Sat 1/3/09	Sat 1/3/09	72	Keith01										
74	4.2.6.6.12 Install Star Wars: Knights of the Old	1 hr	Sat 1/3/09	Sat 1/3/09	73	Keith01										
75	4.2.6.6.13 Windows XP SP3 software installs complete	0 days	Sat 1/3/09	Sat 1/3/09	74	Keith02,Keith01										
76	4.2.6.7 Windows Vista Ultimate x64 software	0.5 days	Sat 1/3/09	Sat 1/3/09												
77	4.2.6.7.1 Install Office 2007	1 hr	Sat 1/3/09	Sat 1/3/09	75	Keith02										
78	4.2.6.7.2 Install Visual Studio 2005	3 hrs	Sat 1/3/09	Sat 1/3/09	77	Keith02										
79	4.2.6.7.3 Install Visual Studio 2008	3 hrs	Sat 1/3/09	Sat 1/3/09	78	Keith02										
80	4.2.6.7.4 Install Java JDK and Eclipse	30 mins	Sat 1/3/09	Sat 1/3/09	79	Keith02										
81	4.2.6.7.5 Install Notepad++	5 mins	Sat 1/3/09	Sat 1/3/09	80	Keith01										
82	4.2.6.7.6 Install Firefox	10 mins	Sat 1/3/09	Sat 1/3/09	81	Keith01										
83	4.2.6.7.7 Windows Vista Ultimate x64 software installs complete	0 days	Sat 1/3/09	Sat 1/3/09	82	Keith02,Keith01										
84	4.3 Monitor system for 24 hours	1 day	Sat 1/3/09	Sat 1/3/09	83	Keith01[67%],Kei										
85	4.4 Sign off on stable system	0 days	Sat 1/3/09	Sat 1/3/09	84											
86	5 Controlling	298.13 days	Sun 11/18/07	Fri 1/2/09												
87	5.1 Study modern architecture	1167.13 days	Sun 11/18/07	Thu 12/11/08												
256	5.2 Status	1218.13 days	Fri 11/23/07	Fri 1/2/09												
316	6 Closing	0 days	Sat 1/3/09	Sat 1/3/09												
317	6.1 Develop and Present Report	2 hrs	Sat 1/3/09	Sat 1/3/09	84	Keith01										
318	6.2 Close Project	0 hrs	Sat 1/3/09	Sat 1/3/09	317	Keith01										



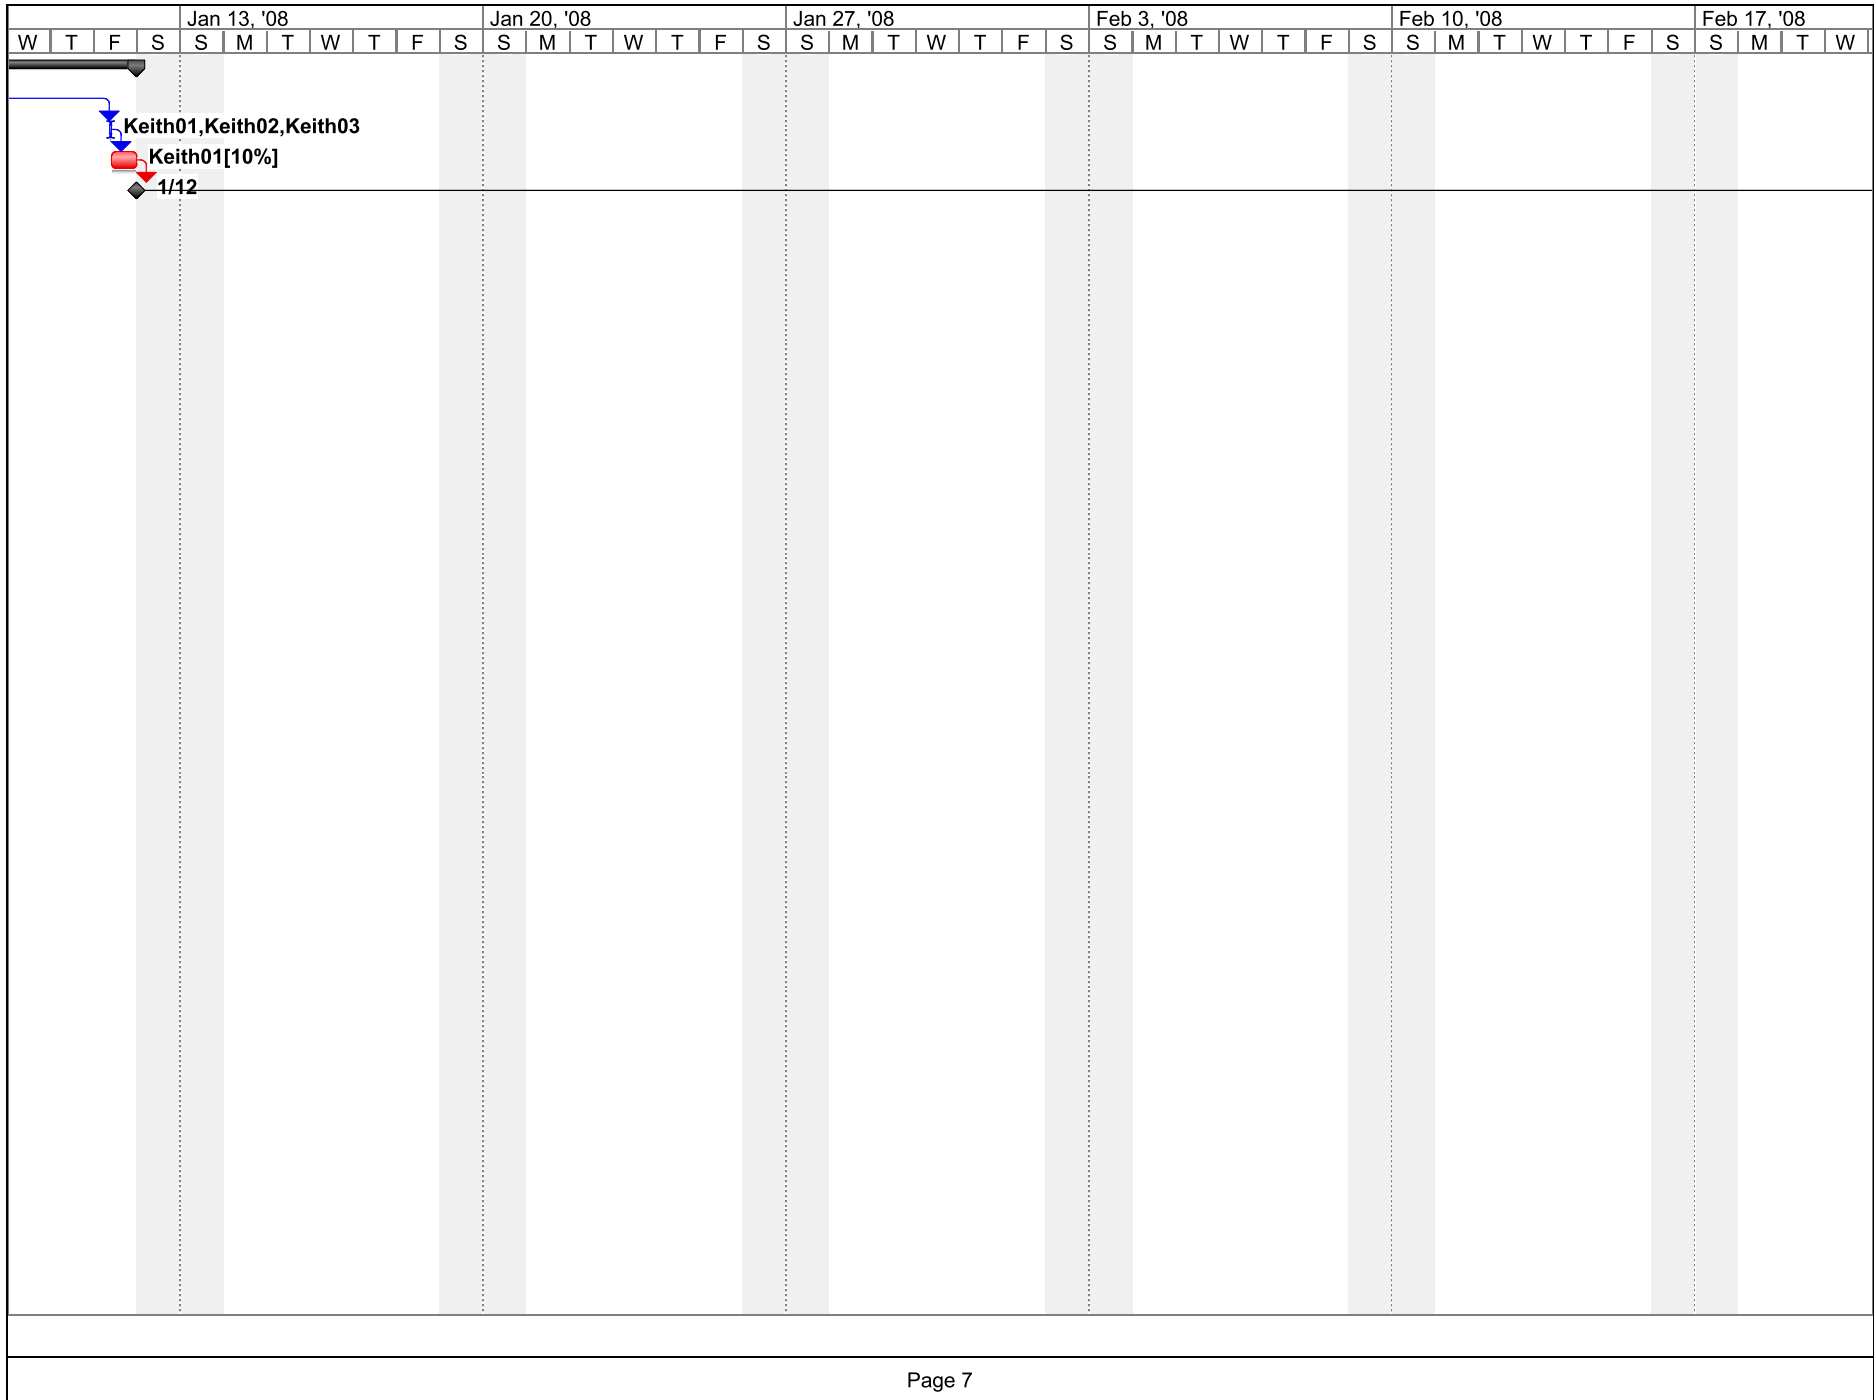

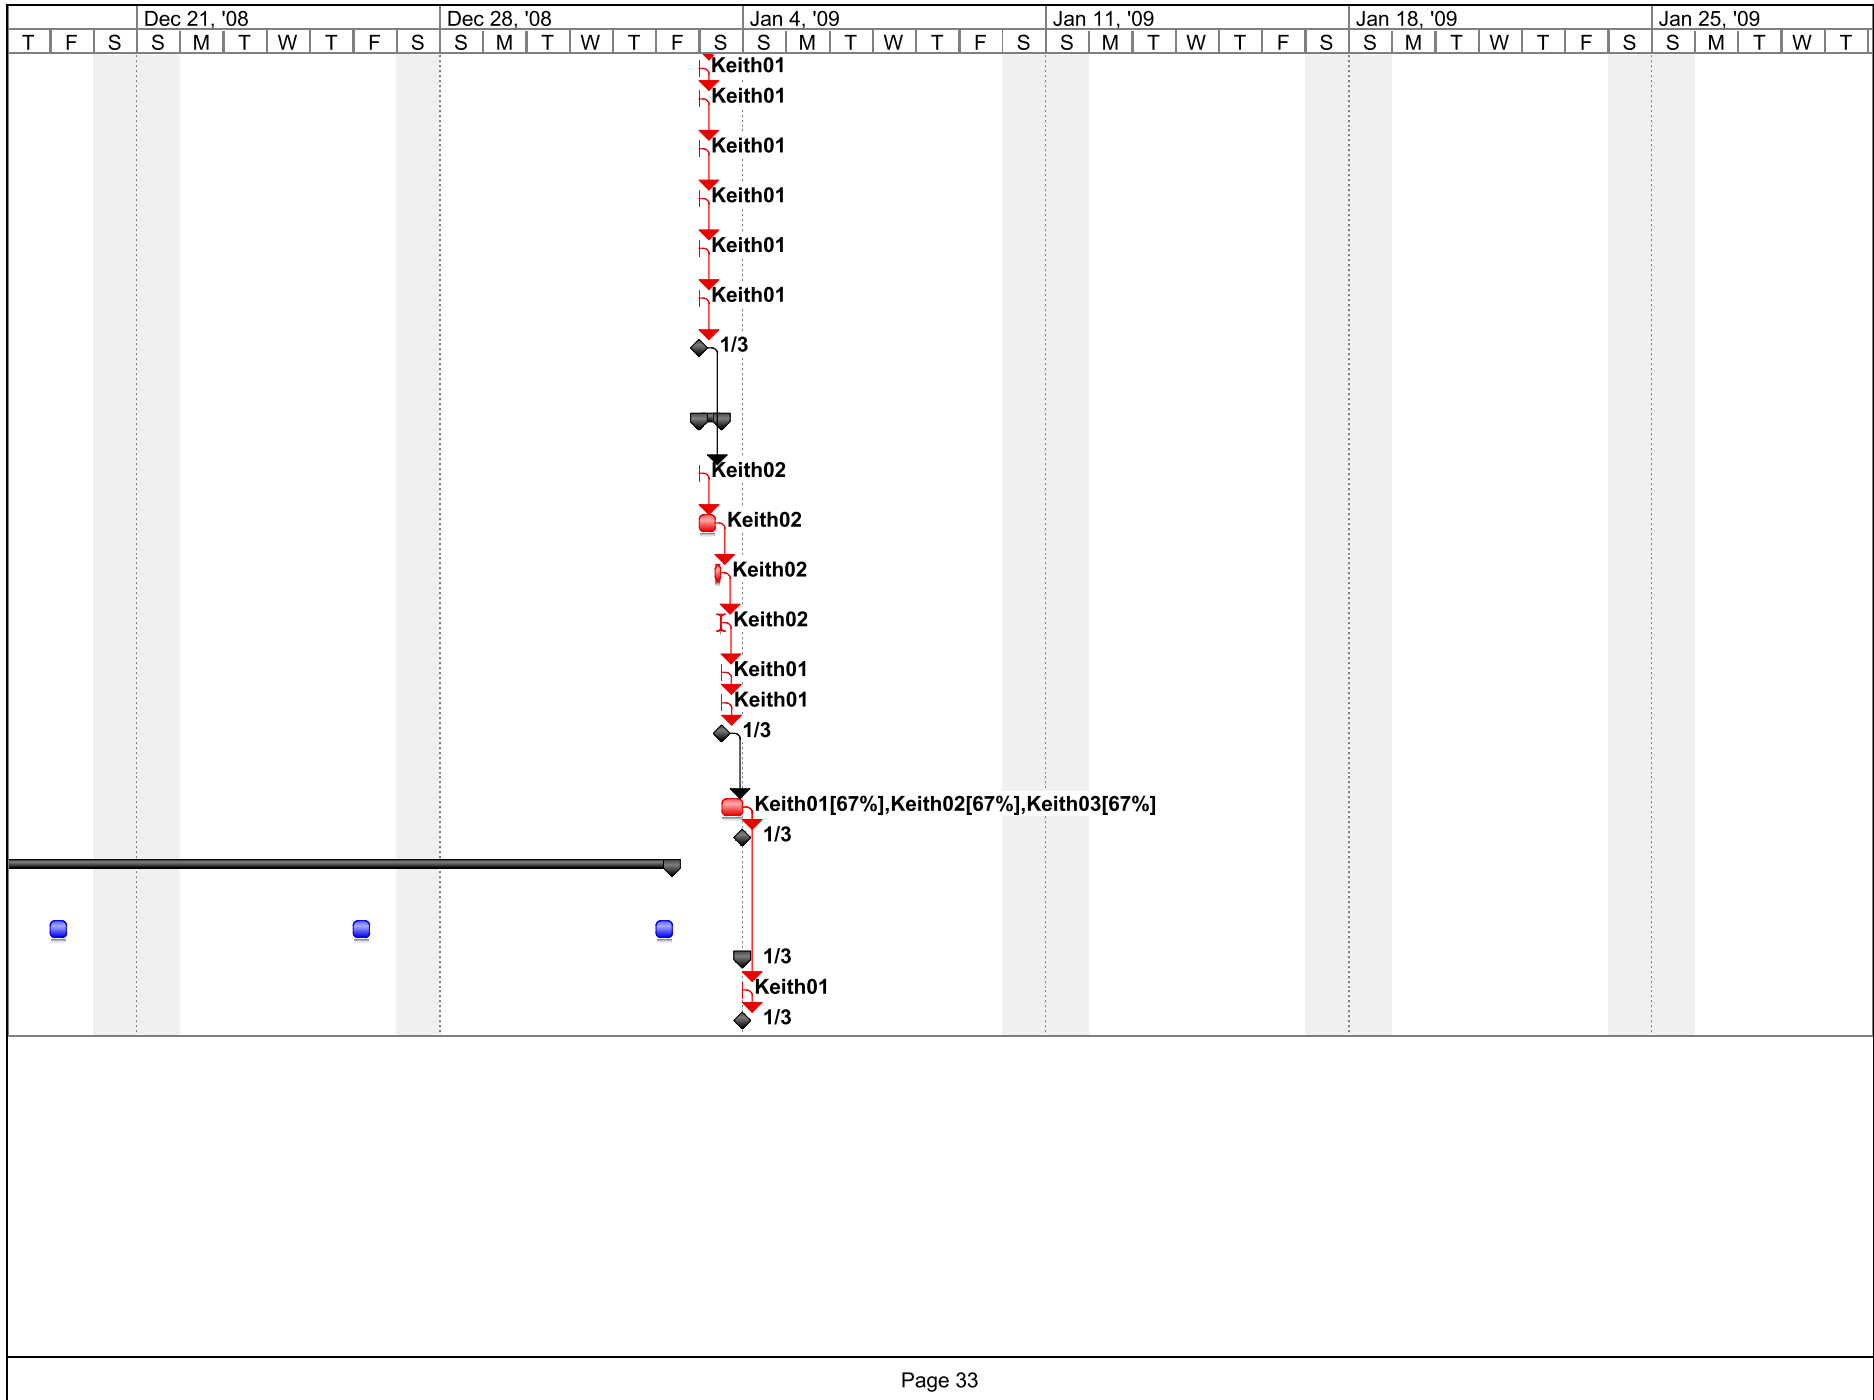










				Nov 9, '08				Nov 16, '08				Nov 23, '08				Nov 30, '08				Dec 7, '08				Dec 14, '08											
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W





Project: Personal PC Update
Date: Mon 5/31/10

Task		Rolled Up Task		External Tasks	
Critical Task		Rolled Up Critical Task		Project Summary	
Progress		Rolled Up Milestone		Group By Summary	
Milestone		Rolled Up Progress		Deadline	
Summary		Split	
